COON CREEK WATERSHED DISTRICT
Request for Board Action

MEETING DATE:	January 26, 2026
AGENDA NUMBER:	12
ITEM:	Ditch 41 Inspection Report

AGENDA:	Discussion
FISCAL IMPACT:	Budgeted

REQUEST
Receive inspection report.

BACKGROUND
This inspection is part of the District's Operations and Maintenance (O&M) program and the National Pollutant Discharge Elimination System (NPDES) requirement of inspecting 20% of the open channels annually.

Ditch 41 is located in Coon Rapids and Blaine.
The channel is 18.5 miles (97,627 feet)
Drainage area is 10.6 square miles (6,815 acres)
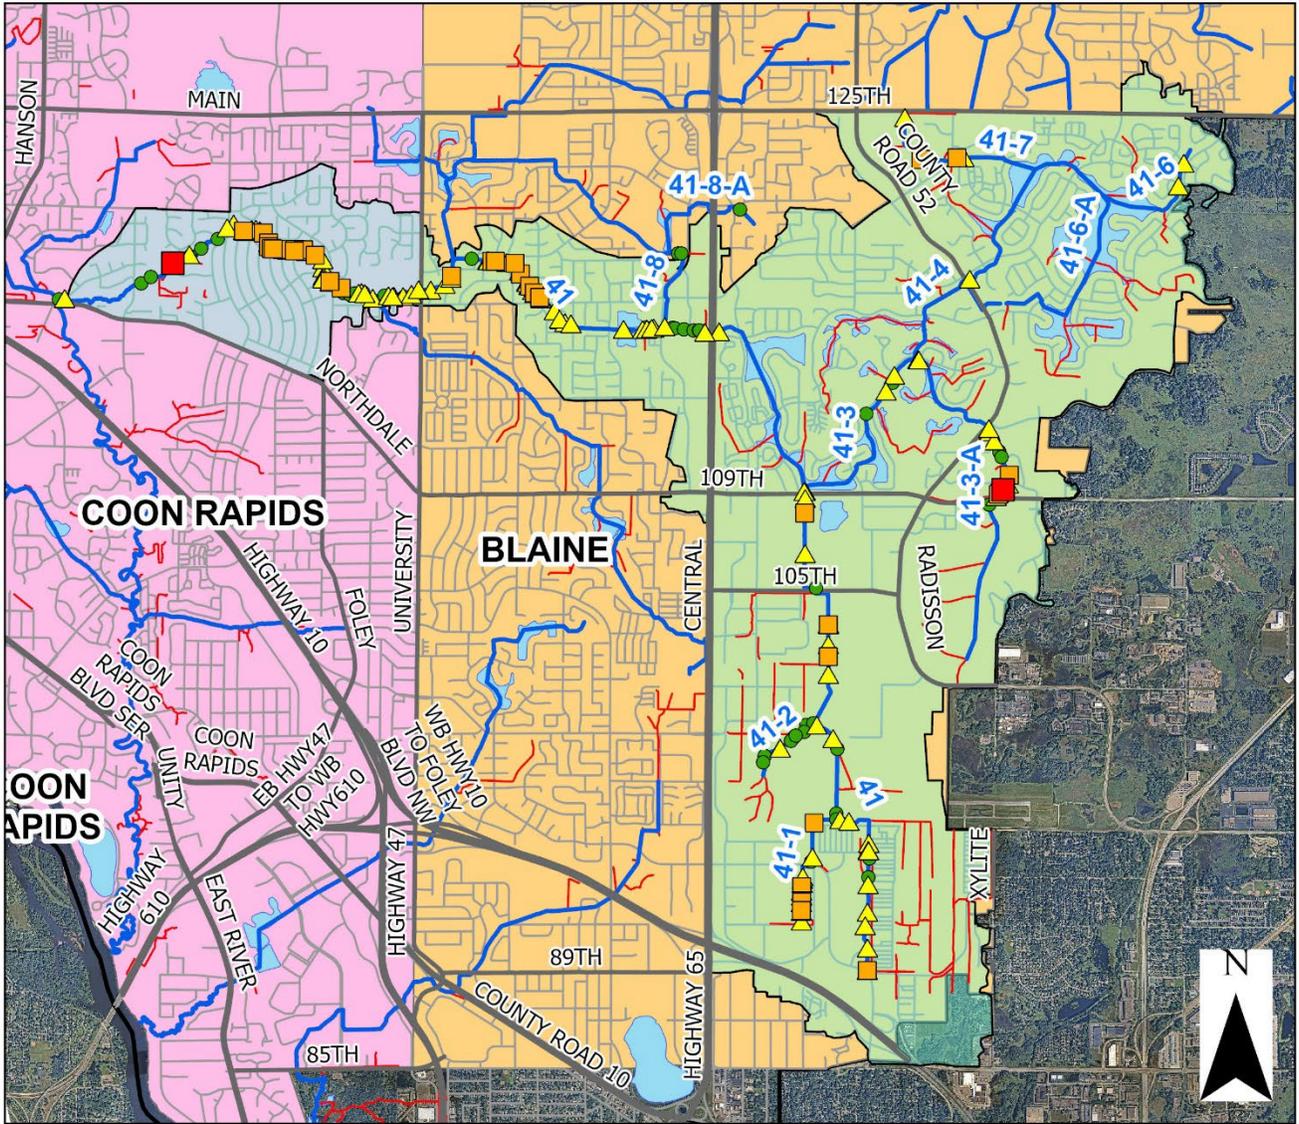11 Public Laterals

IDENTIFIED MAINTENANCE NEEDS

Need	Count	Cost Estimate	Immediate	Repair	Monitor
Obstruction	60	$116,000	$0	$22,000	$94,000
Ditch Repair	14	$52,672	$0	$0	$52,672
Bank Failure	59	$478,450	$3,350	$28,225	$446,875
Illicit Discharge	13	$0	$0	$0	$0
Beaver	2	$0	$0	$0	$0
Other	60	$0	$0	$0	$0
	208	**$647,122**	**$3,350**	**$50,225**	**$593,547**

RECOMMENDATION

1. Receive report.

Ditch 41 General

Legend:

- —— Private Ditch
- —— Public Ditch
- —— Roads
- Subwatershed
- Lakes
- ▭ CCWD Boundary

- ■ Immediate Repair
- ■ Maintenance Req.
- ▲ Monitor
- ● No Problem

- —— Major Roads
- Blaine
- Coon Rapids
